

SAMCO National Construction Co.
76 Al Taya ran St, Nasr City, Cairo, Egypt
Tel: 02 226 245 27
Tel: 02 238 688 16



Ref No.: BD-CW-SAMCO-ACE-LET-STR-056

25- February-2026

To: ACE Project Management | Moharram Bakhoun

Attention: Eng. Abdulaziz Mohamed (Project Manager)

Project Name: The Big Business District.

Contract/Package: Construction Works of the Civil Works for Buildings B1, B2, B3 and B4 – Phase 1.

Subject: Submission of Interim Payment Certificate No. 4

Dear Sir,

With reference to the above-mentioned subject, we hereby submit **Interim Payment Certificate No. 4** for your review and approval.

The submission includes both **soft and hard copies** of the certificate as required.

Attached:

– Interim Payment Certificate No. 4 (Soft & Hard Copies)

Best regards,

Eng./ Mohammed Sami Mohammed
Project Director
SAMCO National Construction



بتاريخ: 2026 /03/4

المرجع : BD-ACEPM-ROYA-LET-012

السادة : شركة رؤية للاستثمار العقاري

عناية : المهندس / مصطفى جلال

اسم المشروع : The BIG

اسم العقد : The BIG -SAMCO

الموضوع : توصيات الخاصة بشأن مستخلص رقم 4- شركة سامكو الوطنية للإنشاءات

تحية طيبة وبعد،،،

بالإشارة الى الموضوع المذكور أعلاه ، مرفق طيه المستخلص الجاري رقم (4) لمشروع The Big (شركة سامكو الوطنية للإنشاءات) عن الاعمال المنفذه حتي تاريخ 2026-2-20 وتمت مراجعته فنيا بقيمه اجمالية (125.728.926.01) جنيه مصري (مائة و خمسة و عشرون مليون و سبعمائة و ثمانية و عشرون ألف و تسعمائة و ستة و عشرون جنيه مصري و واحد قرش فقط لا غير) شاملا ضريبة القيمة المضافة وقد تمت مراجعة المستخلص فنيا وتعاقديا ولا مانع من صرف قيمة المستخلص مع مراعاة ما يلي

1. تطبيق بنود التعاقد

2.مراجعة ما سبق صرفه

وتفضلوا بقبول فائق الاحترام والتقدير...



Ref No.: BD-ACEPM-ROYA-LET-0012

4th of March 2026

To: Roya Developments

Attention: Eng.: Mostafa Galal

Project: The BIG

Package: Construction Works of the Civil Works for Buildings B1, B2, B3 and B4 (The Big)

Subject: ACEPM Recommendation of Monthly Interim Payment No. (4) SAMCO Al-Watanya for Construction

Dear Sir

With reference to the a/m subject, ACEPM hereby draws Roya Development's kind attention to the recommendation made by ACEPM for the Contractor's Interim Payment No.4 with the cut-off date of 20RD February 2026 submitted via letter dated 25th February 2026 as follows:

- The Interim Payment was reviewed by ACE (from a technical point of view) and its assessment was sent to ACEPM via TR NO.0065 dated Monday, 23th of February 2026,
- ACEPM recommendation for the amount due to the Contractor (recommendations of the related Interim Payment Certificate "IPC") is shown in the following table based on the attached supporting particulars: -

Submissions	Gross Amount of Invoice			Net Amount of Invoice		
	Previous	Current	Total	Previous	Current	Total
Contractor's First Submission	79,680,101.10	46,048,824.91	125,728,926.01	50,351,145.66	28,067,998.19	78,419,143.85
Contractor's Second Submission	N/A	N/A	N/A	N/A	N/A	N/A
ACEPM's Recommendations	79,680,101.10	46,048,824.91	125,728,926.01	50,351,145.66	25,053,696.48	75,404,842.14

- An amount of (10,572,504.50) EGP. has been deducted from the work certified due to non-submission from SAMCO of the BOQ breakdown,

Yours faithfully
Eng / Abdelaziz Mohamed

Project Director
ACEPM

Attachments: As Enclosed.

Project Information			
Project Name	The big	The Accepted Contract Amount	367,286,025
Employer	ROYA	Contractor name/scope	Samco Al-Wataniya for Construction
Engineer	ACE CONSULTANT	Cut of Date	February 20/2026
Project Manager	ACE project Management	IPC No	4
Contract Type /NO	Roya-Big-2025-01	Contract Start Date	11-Sep-25
		Contract End Date	10-Apr-27

Contractual Terms		
	Item	Amount
A	Accepted Contract Amount	367,286,025.00
B	Accepted variation Amount	
D= Revised Contract Sum " A + B " =		367,286,025.00

Advance payment conditions		
	Item	Amount
A	Advanced Payment	91,821,506.25
B	Recovery for Advanced Payment	27,572,132.90
C= Advanced Payment Balance " A + B " =		64,249,373.35

Payment Details		A	B = C - A	C
		Previous Work Certified	Current Amount	Work Certified To-Date
A-	Certified steel Work Volume of Accepted contract	54,555,318.54	40,393,706.06	94,949,024.60
B-	Certified Work Volume of Variation Order	15,339,506.99	-	15,339,506.99
C-	Certified Price Variance	-	-	-
E= Total Work Certified excluding VAT " A + B + C " =		69,894,825.53	40,393,706.06	110,288,531.59
F=VAT		9,785,275.57	5,655,118.85	15,440,394.42
G=Total Work Certified including VAT " E + F " =		79,680,101.10	46,048,824.91	125,728,926.01

H= Material on site					
Deductions:					
J=E*(x%)	Retention	5%	3,494,741.28	2,019,685.30	5,514,426.58
K=E*(x%)	Advance payment	25%	17,473,706.38	10,098,426.51	27,572,132.90
L=E*(x%)	Withholding Tax	1.00%	698,948.26	403,937.06	1,102,885.32
M=E*(x%)	Social Insurance	5.00%	3,494,741.28	2,019,685.30	5,514,426.58
N	Other Deductions/back charges		32,333.00	15,375.00	47,708.00
N'=VAT Retention Amount			4,134,485.25	6,438,019.25	10,572,504.50
O =Total Deductions= sum (J:N') =			29,328,955.44	20,995,128.43	50,324,083.87
P=Total due amounts " G + H -O" =			50,351,145.66	25,053,696.48	75,404,842.14

Previous paid	18,299,639.00
Net Payment	57,105,203.14
Amounts in words	Fifty-seven million, one hundred and five thousand, two hundred and three Egyptian pounds and fourteen piastres only.

Certifications:			The Consultant		
The Contractor			The Employer		
Project Manager	Technical Office manager	Cost Control Engineer	Project Manager	Cost Control manager	Cost Control Engineer
Name:	Name:	Name:	Name:	Name:	Name:
Signature:	Signature:	Signature:	Signature:	Signature:	Signature:
Date:	Date:	Date:	Date:	Date:	Date:
the Project Manager			the Employer		
Project Manager	Cost Control manager		Project Manager	Commercial Director	Cost Control Manager
Name:	Name:		Name:	Name:	Name:
Signature:	Signature:		Signature:	Signature:	Signature:
Date:	Date:		Date:	Date:	Date:

Project Information

Project Name	The big	The Accepted Contract Amount	367,286,025
Employer	ROYA	Contractor name/scope	Samco Al-Wataniya for Construction
Engineer	ACE CONSULTANT	Cut of Date	February 20/2026
Project Manager	ACE project Management	IPC No	4
		Contract Start Date	11-Sep-25
Contract Type /NO	Roya-Big-2025-01	Contract End Date	10-Apr-27

Contractual Terms

	Item	Amount
A	Accepted Contract Amount	367,286,025.00
B	Accepted variation Amount	
D= Revised Contract Sum " A + B " =		367,286,025.00

Advance payment conditions

	Item	Amount
A	Advanced Payment	91,821,506.25
B	Recovery for Advanced Payment	27,572,132.90
C= Advanced Payment Balance " A + B " =		64,249,373.35

		A	B = C - A	C
Payment Details		Previous Work Certified	Current Amount	Work Certified To-Date
A-	Certified steel Work Volume of Accepted contract	54,555,318.54	40,393,706.06	94,949,024.60
B-	Certified Work Volume of Variation Order	15,339,506.99	-	15,339,506.99
C-	Certified Price Variance	-	-	-
B= Total Work Certified excluding VAT " A+B+C " =		69,894,825.53	40,393,706.06	110,288,531.59
F=VAT		9,785,275.57	5,655,118.85	15,440,394.42
G= Total Work Certified including VAT " E + F " =		79,680,101.10	46,048,824.91	125,728,926.01
H= Material on site				
Deductions:				
J=E*(x%)	Retention 5%	3,494,741.28	2,019,685.30	5,514,426.58
K=E*(x%)	Advance payment 25%	17,473,706.38	10,098,426.51	27,572,132.90
L=E*(x%)	Withholding Tax 1.00%	698,948.26	403,937.06	1,102,885.32
M=E*(x%)	Social Insurance 5.00%	3,494,741.28	2,019,685.30	5,514,426.58
N	Other Deductions/back charges	32,333.00	15,375.00	47,708.00
N*=VAT Retention Amount		4,134,485.25	6,438,019.25	10,572,504.50
O =Total Deductions= sum (J:N*) =		29,328,955.44	20,995,128.43	50,324,083.87
P=Total due amounts " G + H -O " =		50,351,145.66	25,053,696.48	75,404,842.14
Previous paid				18,299,639.00
Net Payment			57,105,203.14	
Amounts in words		Fifty-seven million, one hundred and five thousand, two hundred and three Egyptian pounds and fourteen piastres only.		

Certifications:					
The Contractor			the Consultant		
Project Manager	Technical Office manager	Cost Control Engineer	Project Manager	Cost Control manager	Cost Control Engineer
Name:	Name:	Name:	Name:	Name:	Name:
Signature:	Signature:	Signature:	Signature:	Signature:	Signature:
Date:	Date:	Date:	Date:	Date:	Date:
the Project Manager			the Employer		
Project Manager	Cost Control manager		Project Manager	Commercial Director	Cost Control Manager
Name:	Name:		Name:	Name:	Name:
Signature:	Signature:		Signature:	Signature:	Signature:
Date:	Date:		Date:	Date:	Date:

367286025.00	القيمة	The Big	اسم المشروع
Samco Al-Wataniya for Construction	المالك	ROYA	العميل
February 20/2026	تاريخ البدء	ACE CONSULTANT	الاستشاري
4	رقم المستخلص	ACE project Management	مدير المشروع
11-Sep-25	تاريخ بدء العقد		
10-Apr-27	تاريخ انتهاء العقد	Roya-Big-2025-01	نوع العقد / رقم

القيمة	القيمة	القيمة	القيمة
367,286,025.00	A	B	
367,286,025.00	B	A + B =	

القيمة	القيمة	القيمة	القيمة
91,821,506.25	A	B	
27,572,132.90	B	A + B =	
64,249,373.35			

C	B = C - A	A	التفصيل المستخلص
القيمة الاصل	القيمة الاصل الحالية	القيمة الاصل السابقة	
94,949,024.60	40,393,706.06	54,555,318.54	A - قيمة الاصل القديم
15,339,506.99	-	15,339,506.99	B - قيمة اموال التغيير
			C - قيمة فروق الاسعار
110,288,531.59	40,393,706.06	69,894,825.53	E = A + B + C =
15,440,394.42	5,655,118.85	9,785,275.57	F - ضريبة القيمة المضافة
125,728,926.01	46,048,824.91	79,680,101.10	G = E + F =
			H - اصل تكاليف الخدمات في الموقع

الخصومات والاستقطاعات	القيمة	القيمة	القيمة	القيمة
5%	5,514,426.58	2,019,685.30	3,494,741.28	J = E * (x%)
25%	27,572,132.90	10,098,426.51	17,473,706.38	K = E * (x%)
1.00%	1,102,885.32	403,937.06	698,948.26	L = E * (x%)
5.00%	5,514,426.58	2,019,685.30	3,494,741.28	M = E * (x%)
	47,708.00	15,375.00	32,333.00	N - الخصومات الأخرى
	10,572,504.50	6,438,019.25	4,134,485.25	O - نقطة لحوصل تقديم تسهيل سعر المشروع
	50,324,083.87	20,995,128.43	29,328,955.44	P = sum (J-N) =
	75,404,842.14	25,053,696.48	50,351,145.66	Q = G + H - O =
	18,299,639.00			
	57,105,203.14			

Certifications: The Contractor Project Manager Name: <i>Egyptian</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i> Technical Engineer Name: <i>Azthe Big</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i>	the Consultant Project Manager Name: <i>[Signature]</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i> Cost Control manager Name: <i>[Signature]</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i> Cost Control Engineer Name: <i>[Signature]</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i>
the Project Manager Project Manager Name: <i>[Signature]</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i> Cost Control manager Name: <i>Shaymaa Hamdi</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i>	the Employer Project Manager Name: <i>[Signature]</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i> Commercial Director Name: <i>[Signature]</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i> Cost Control Manager Name: <i>[Signature]</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i>

<u>الخصومات والاستقطاعات</u>					
5,514,426.58	2,019,685.30	3,494,741.28	5%	$f = E \times (x\%)$ نفين الاصل (%)	
27,572,132.90	10,098,426.51	17,473,706.38	25%	$K = E \times (x\%)$ القسمة المقننة	
1,102,885.32	403,937.06	698,948.26	1.00%	$L = E \times (x\%)$ حصرية خصم الأرباح التجارية	
5,514,426.58	2,019,685.30	3,494,741.28	5.00%	$M = E \times (x\%)$ الخصومات الاجتماعية	
47,708.00	15,375.00	32,333.00		N الخصومات الأخرى	
10,572,504.50	6,438,019.25	4,134,485.25		$N^+ =$ نقطة لحيث تقديم تحصيل سعر المشروع	
50,324,083.87	20,995,128.43	29,328,955.44		$\text{sum } (j:N^+) =$ إجمالي الخصومات والاستقطاعات = 0	
75,404,842.14	25,053,696.48	50,351,145.66		$= -O + G + H$ " القيمة المتحقق صرفها P=	
18,299,639.00					ما سبق صرفه
	57,105,203.14				قيمة المستطاع الخارج
					قيمة المكتوب به صرفها كالتالي
					قيمة وخمسون مليوناً ومئة وخمسة آلاف ومئتان وثلاثة جنيهات مصرية وأربعة عشر قرشاً فقط لا غير

Certifications: The Contractor Project Manager: <i>Eng. Mohamed Sami</i> Name: <i>Eng. Mohamed Sami</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i>			the Consultant Project Manager Name: Signature: Date:		
the Project Manager Project Manager Name: <i>[Signature]</i> Signature: <i>[Signature]</i> Date: <i>[Date]</i>			the Employer Project Manager Name: Signature: Date:		



Item no.	Description of Works	Unit	Accepted Contract Amount			General Requirements							Remarks
			Qty.	Unit Rate	Total Amount	Quantities			progress %	Total Amount			
						Prev.	Current	Total		Prev.	Current	Total	
	DIVISION 2: SITE CONSTRUCTION												
	Site Clearance General Site clearing, grabbing and demolishing of obstacles with off-site disposal												
2	Excavation and Earthwork												
2.1	Excavation in ordinary soil for depth as per soil investigation report including transporting the excavation materials to the public dumping areas and getting ride of any excavation disposals	m3	0.00	180.00	-	2,989.04	0.00	2,989.04	100%	538,027.20	0.00	538,027.20	
2.2	Excavation in rock for depth as per soil investigation report including transporting the excavation materials to the public dumping areas and getting ride of any excavation disposals	m3	0.00	450.00	-	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2.3	Replacement Soil in accordance with the geotechnical report recommendations including all compaction and necessart tests	m3	12000.00	633.00	7,596,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2.5	Back filling above the foundation and below slab on grade with siliceous clean sand installed in successive lifts, 0.25m thick compacted to not less than 95% using modified Proctor test	m3	6800.00	460.00	3,128,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	DIVISION 3: CONCRETE												
	Structural Concrete Supply and install concrete, including Furnishing, installing materials, concrete materials, aggregate, water, mixing, additives, grading and trowelling, Fiber reinforcement, substrate preparation, protection, covering, cleaning, repairing of defective screed, and any other required items as per Drawings and Snarificatione												
1	03300 Plain Concrete (PC) Grade 200 kg/cm² of OPC and minimum cement content 250 kg/ m³ Blinding layer 300mm thickness		2230.00	3625.00	8,083,750.00	2,018.23	0.00	2,018.23	100%	7,316,083.75	0.00	7,316,083.75	
	03300 Reinforced concrete (RC) Grade 350 kg/cm2 of OPC and minimum cement content 400 kg/m³												
1	Raft Foundation	m3	6550.00	7210.00	47,225,500.00	1,867.57	1,596.08	3,463.64	100%	13,465,158.79	11,507,705.80	24,972,864.59	
2	Retaining Walls	m3	790.00	9900.00	7,821,000.00	0.00	71.70	71.70	100%	0.00	709,790.40	709,790.40	
3	Tanks	m3	800.00	9400.00	7,520,000.00	198.39	0.00	198.39	100%	1,864,847.20	0.00	1,864,847.20	
4	Columns & Walls below SOG	m3	100.00	9100.00	910,000.00	0.00	33.67	33.67	100%	0.00	306,421.66	306,421.66	
	03300 Reinforced concrete (RC) Grade 300 kg/cm2 of OPC and minimum cement content 300 kg/m³												
1	Columns	m3	1560.00	9470.00	14,773,200.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2	slabs	m3	10500.00	9580.00	100,590,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
3	Beams	m3	215.00	9675.00	2,080,125.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
4	Shear walls	m3	1590.00	9465.00	15,049,350.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
5	Stairs	m3	260.00	9360.00	2,433,600.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	03300 Reinforced concrete (RC) Grade 250 kg/cm2 of OPC and minimum cement content 300 kg /m³												
1	Slab on grade 150mm thickness	m2	6370.00	1550.00	9,873,500.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	Deformed high yield steel bars with Different nominal size Used in Raft, Rc Columns, Rc Slabs and all concrete Items	ton	3300.00	40620.00	134,046,000.00	699.01	686.11	1,385.12	100%	28,393,583.10	27,869,788.20	56,263,371.30	
	Fence												
1	Precast concrete fence With Height 2.5 m	l.m	0.00	6500.00	-	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2	Corrugated sheet fence	l.m	0.00	3500.00	-	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	DIVISION 7: THERMAL AND MOISTURE PROTECTION												
	07130 SHEET WATERPROOFING												
	Supply and install sheet waterproofing including furnishing materials, protection mat, sealants and sheet flashing, preparation of substrates, cutting, rounding, intersections, prime coat, and side overlapping to vertical surfaces, reglets and bending free edge in grooving, testing, replacing of damaged membrane, protection, covering and cleaning, and any other required items as per Drawings and Specifications												
1	SBS water prooting memorane of a minimum thickness 4.0mm including protection board for vertical surfaces and protection screed for horizontal surfaces and all needed precautions, accessories, and material as per manufacturing requirements.	m2	9500.00	450.00	4,275,000.00	6,616.93	0.00	6,616.93	100%	2,977,618.50	0.00	2,977,618.50	
	07140 COLD FLUID-APPLIED WATERPROOFING												
	Supply and install Cold applied waterproofing including furnishing materials, protection mat, sealants and sheet flashing, preparation of substrates, cutting, rounding, intersections, prime coat, and side overlapping to vertical surfaces, reglets and bending free edoe in grooving, testing, replacino of damaoed membrane.												
1	Cold applied damp-proofing for top side of raft and underground concrete surfaces in contact with soil/backfill,	m2	7,600.00	90.00	684,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2	Cold applied Crystalline Waterproofing for water tanks	m2	1,900.00	630.00	1,197,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	Total Amount of Work				367,286,025.00					54,555,318.54	40,393,706.06	94,949,024.60	

ROY



ACE-PM
MOHARRAM BAKHOUM

PRIME
CONSULTING OFFICE



Item no.	Description of Works	Unit	Accepted Contract Amount			General Requirements							Remarks	
			Qty.	Unit Rate	Total Amount	Quantities			progress %	Total Amount				
						Prev.	Current	Total		Prev.	Current	Total		
	Variation Order : (BD-CW-SAMCO-ACE-VOR-001-R00)													
	Earthwork													
1	By m3, Replacement Layer Supply and Installation of a 2:1 mix of crushed stone and clean sand to the specified thickness and levels as per the drawings and Engineer's directions. The material is to be applied in layers not exceeding 25 cm loose thickness, moisture-conditioned, and mechanically compacted to achieve the required compaction as per project specifications and geotechnical recommendations.	m3	12000.00	792.28	9,507,360.00	10,293.689	0.000	10,293.689	100%	8,155,483.76	0.00	8,155,483.76		
2	By m2, supplying and installing two layers of TX160 geogrid with a tensile strength of 40 kN/m, and a 10 cm high geocell layer, as per the levels indicated in the construction drawings and soil recommendation report. The rate excludes earthworks or backfilling inside the geocell.	m2	7850.00	1104.84	8,672,994.00	6,502.320	0.00	6,502.320	100%	7,184,023.23	0.00	7,184,023.23		
Total Amount of Work					18,180,354.00					15,339,506.99	0.00	15,339,506.99		
Technical Director SAMCO THE BIG Signature Date:														

Signature





Samco-National Construction Company
Project: The Big Project
(progress of the First Invoice for the big Proj)




Item	Description	Unit	QS NO	Progress Percentage	Notes
B.O.Q ITEMS					
Excavation	Excavation in ordinary soil for depth as per soil investigation report including transporting the excavation materials to the public dumping areas and getting ride of any excavation disposals	m3	QS-SUR-001	100%	The quantity is approved and executed at 100% as per the As-Built Implementation
			QS-SUR-002	100%	
			QS-SUR-004-R01	100%	
PC	03300 Plain Concrete (PC) Grade 200 kg/cm² of OPC and minimum cement content 250 kg/m³ Blinding layer 300mm thickness	m3	QS-STR-01	89%	According to the attached drawings
RC (RAFT)	(03300) Reinforced concrete (RC) Grade 350 kg /cm2 of OF OPC and minimum cement content 400 kg/m3	m3	QS-STR-03&06	87%	According to the attached drawings (Form work)
				64%	According to the attached drawings (reinforcement)
				60%	According to the attached drawings (Casting)
RC (R.W Below s.o.g)	(03300) Reinforced concrete (RC) Grade 350 kg /cm2 of OF OPC and minimum cement content 400 kg/m3	m3	QS-STR-11	100%	According to the attached drawings (Form work&reinforcement&casting)
RC (col Below s.o.g)	(03300) Reinforced concrete (RC) Grade 350 kg /cm2 of OF OPC and minimum cement content 400 kg/m3	m3	QS-STR-12&13	100%	According to the attached drawings (Form work&reinforcement&casting)
Membrane SBS	SBS Water proofing membrane of a minimum thickness 4.0mm including protection board for vertical surfaces and protection screed for horizontal surfaces and all needed precautions, accessories, and material as per manufacturing requirements.	m2	QS-STR-04	89%	According to the attached drawings
Steel	Deformed high yield steel bars with Different nominal size Used in Raft, Rc Columns, Rc Slabs and all concrete Items	ton	MIR-STR-015&MIR-STR-050&MIR-STR-056rev01&MIR-STR-057rev01&MIR-STR-058rev01	100%	According to the approved MIR
			MIR-STR-61&MIR-STR-62&MIR-STR-63&MIR-STR-64&MIR-STR-65&MIR-STR-66&MIR-STR-67&MIR-STR-68&MIR-STR-69&MIR-STR-70&MIR-STR-71	100%	According to the approved MIR
Variation Orders ITMES					
Soil Replacement	By m3, Replacement Layer Supply and Installation of a 2:1 mix of crushed stone and clean sand to the specified thickness and levels as per the drawings and Engineer's directions. The material is to be applied in layers not exceeding 25 cm loose thickness, moisture-conditioned, and mechanically compacted to achieve the required compaction as per project specifications and geotechnical recommendations.	m3	QS-SUR-005	100%	The quantity is approved and executed 100% as per the As-Built Implementation
			QS-SUR-006-rev01	100%	The quantity is approved and executed 100% as per the As-Built Implementation
Geogride & geocell	By m2, supplying and installing two layers of TX160 geogrid with a tensile strength of 40 kN/m, and a 10 cm high geocell layer, as per the levels indicated in the construction drawings and soil recommendation report. The rate excludes earthworks or backfilling inside the geocell.	m2	QS-STR-02	88%	According to the attached drawings

Consultant



Mohammed Bakhoum

casting Col below s.o.g

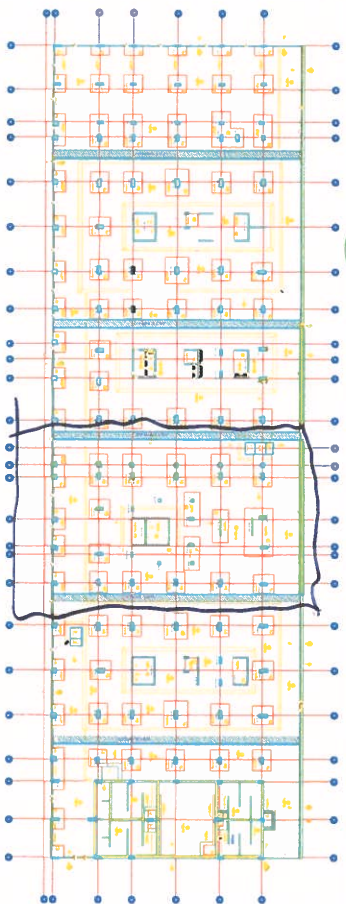

تم صب رقاب ٩ عدد ب (B3) حتى مستوى (+205)




%100

Work
casting
completed



form work & Rnf col below s.o.g

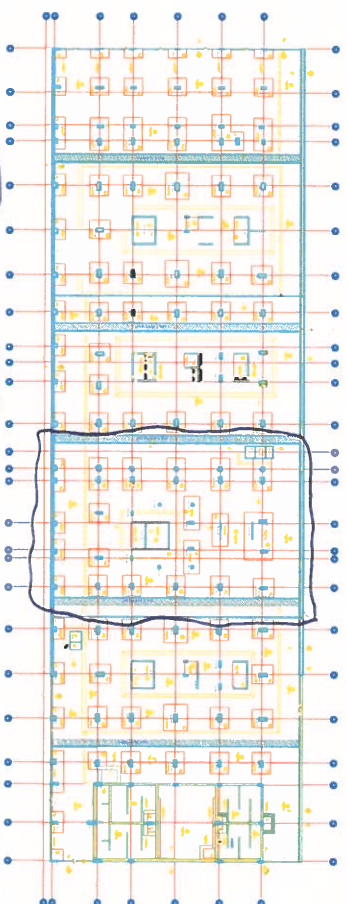

تم اكتمال عمل حديد رقب ٩ عدد ب (B3) حتى مستوى (+205)



%100




Work
completed

Eng / Omar in answer

4/4




Membrane Insulation




✓

P.C



✓

TX-160 & GEOCELL-10CM

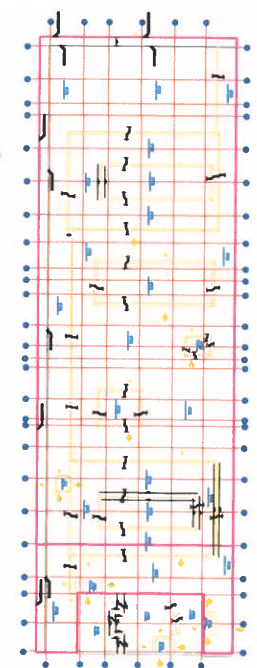


✓



Eng / amr mawda


1/14

casting raft

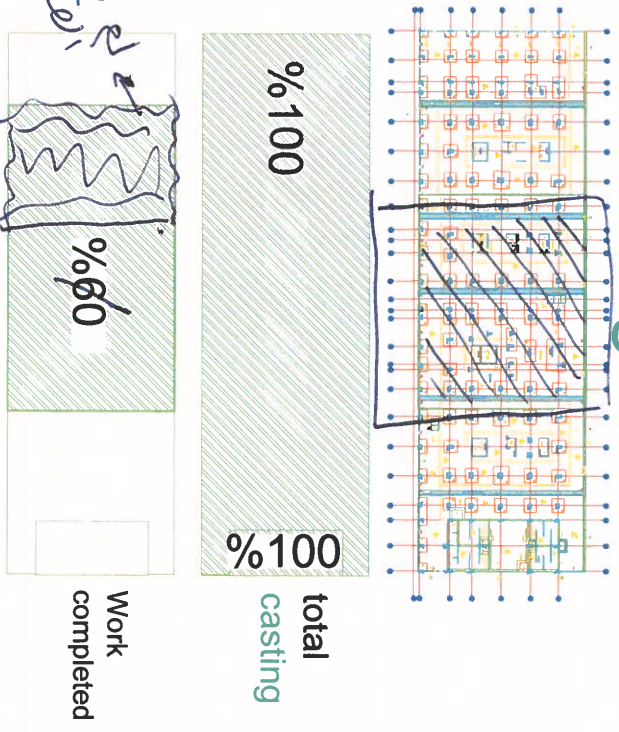


كم صب شرائح صان B2, B3 مسكور (16-17) الانكور (24-25)

reinforcement raft

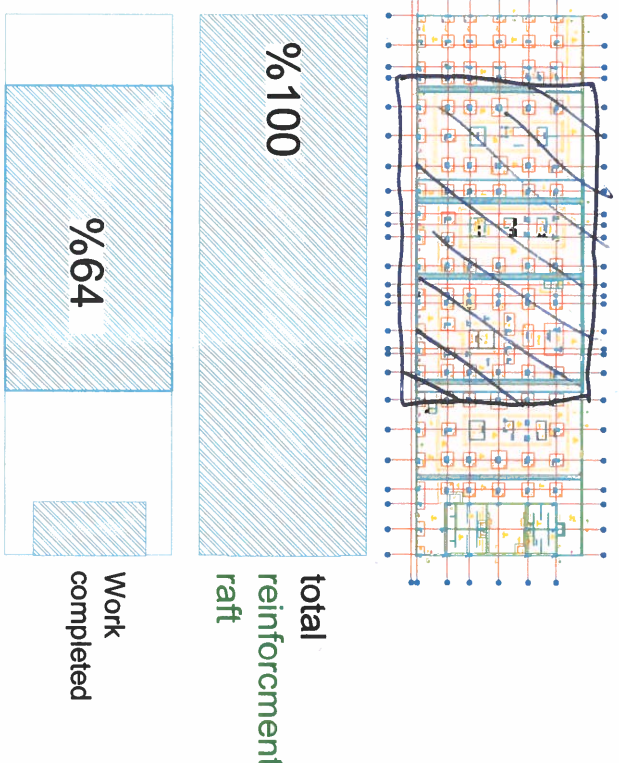

كم اسلام اعمال حدة الانكور مسكور (12) الانكور (24) (B1, B2, B3)

Form work raft

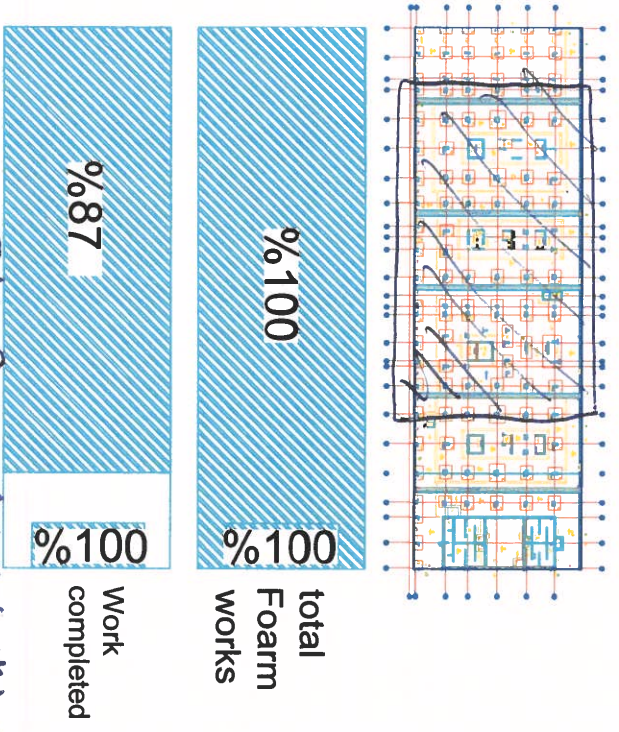


كم اسلام اعمال صب (ك البنية المثلج) مسكور (12), (14) (24) لهذا B1, B2, B3

Eng / Omar Mawser



2/14

casting R.w below s.o.g

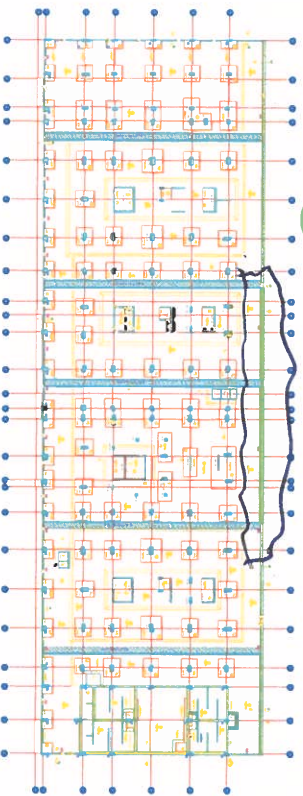


%100

Work
casting
completed

تم صبها ~~في~~ ساند ألى كور (B2)
(17) إالى كور (24) حشاشيسو ب 205.0
(B2+B3)



form work & Rnf R.w below s.o.g

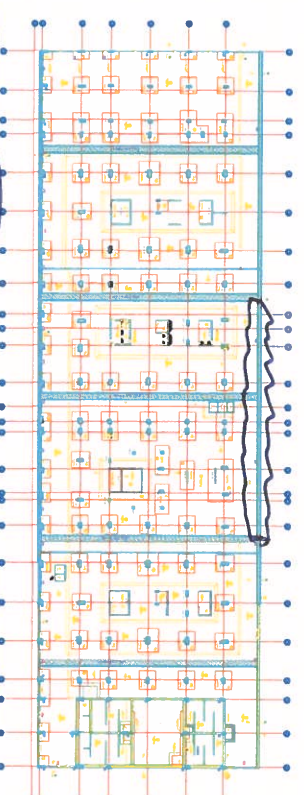

%100

Work
completed

تم إنشائهم أعمال الحماركة والبيتة رة للخط 17 ألى كور
(17) حشاشيسو ب 205 (24) ففم حشاشيسو ب 205

Eng / amr morsa..

3/14
