

Ref No.: BD-CW-SAMCO-ACE-LET-STR-064

02- April- 2026

To: ACE Project Management | Moharram Bakhoun
Attention: Eng. Abdulaziz Mohamed (Project Manager)

Project Name: The Big Business District.

Contract/Package: Construction Works of the Civil Works for Buildings B1, B2, B3 and B4 – Phase 1.

Subject: Notification of claim Due to Delay in Technical Clarifications.

Dear Sir,

With reference to the ongoing work plan on site, and due to the delay in responding to RFI No. (3, 4, 5) sent on 08/03/2026, as well as RFI No. (6), which Was sent seeking clarification on your response to RFI No (2).

we would like to bring to your attention that no activites of works in the water tank, basement sum pits, and the electrical works in the staircases with in the next two days.

We also wish to emphasize that we will take the necessary actions to claim an extension of time and cost resulting from this delay, in accordance with the contract sub Clause.

Therefore, we kindly request your urgent response to the mentioned queries, so that work can resume at the Earliest possible time.

Attached: Photos of the halted works on site for your reference.

With sincere regards and appreciation,

Eng./ Mohammed Sami Mohammed
Project Director
SAMCO National Construction



Ref No.: BD-CW-SAMCO-ACE-LET-STR-064

02- April- 2026

To: ACE Project Management | Moharram Bakhoun

Attention: Eng. Abdulaziz Mohamed (Project Manager)

Project Name: The Big Business District.

Contract/Package: Construction Works of the Civil Works for Buildings B1, B2, B3 and B4 – Phase 1.

Subject: Notification of claim Due to Delay in Technical Clarifications.

Dear Sir,

With reference to the ongoing work plan on site, and due to the delay in responding to RFI No. (3, 4, 5) sent on 08/03/2026, as well as RFI No. (6), which Was sent seeking clarification on your response to RFI No (2).

we would like to bring to your attention that no activites of works in the water tank, basement sum pits, and the electrical works in the staircases with in the next two days.

We also wish to emphasize that we will take the necessary actions to claim an extension of time and cost resulting from this delay, in accordance with the contract sub Clause.

Therefore, we kindly request your urgent response to the mentioned queries, so that work can resume at the Earliest possible time.

Attached: Photos of the halted works on site for your reference.

With sincere regards and appreciation,

Eng./ Mohammed Sami Mohammed
Project Director
SAMCO National Construction



DIGITAL PHOTO ATTACHED 1




DIGITAL PHOTO ATTACHED 2




DIGITAL PHOTO ATTACHED 3



DIGITAL PHOTO ATTACHED 4

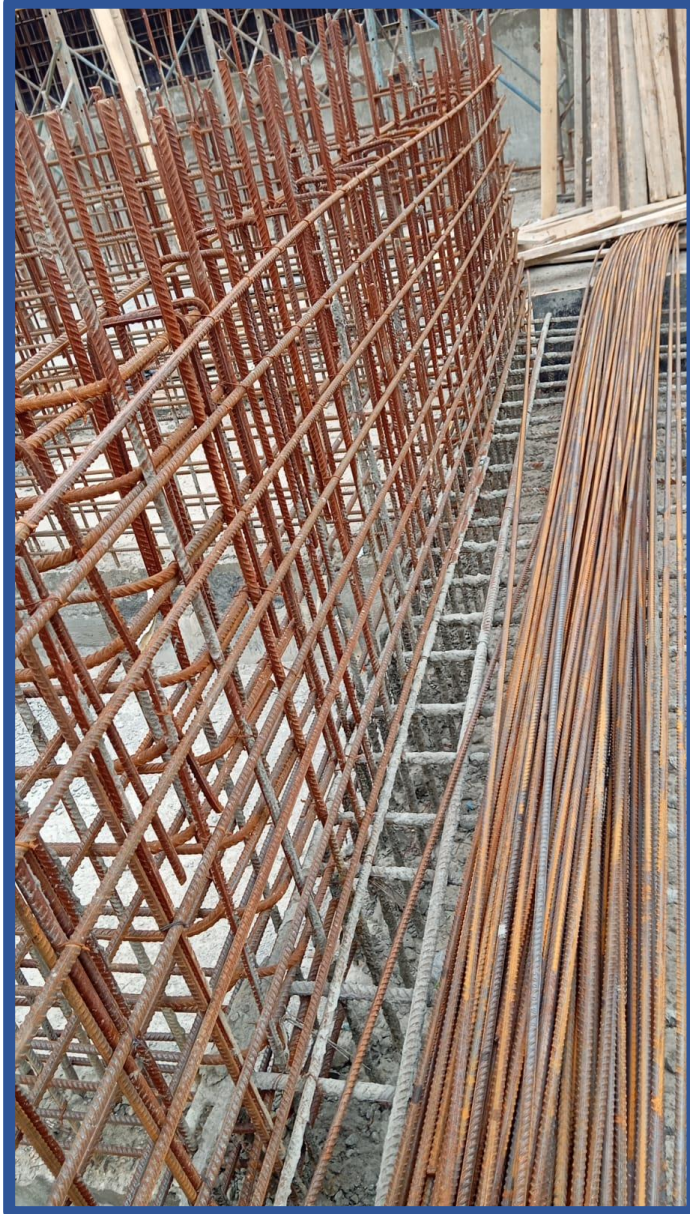

DIGITAL PHOTO ATTACHED 6

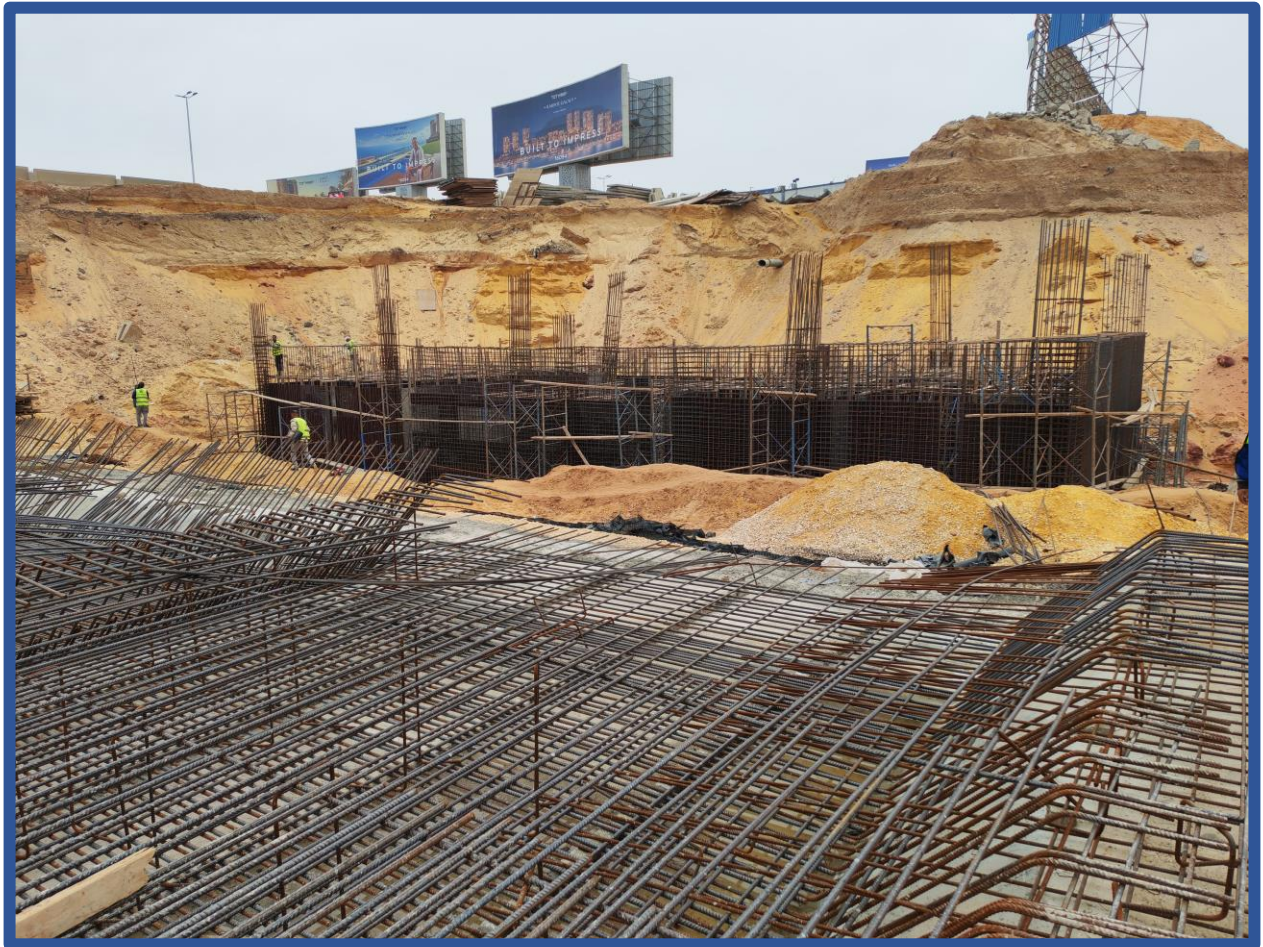

Request for Information (RFI)

Project:	The Big Business District	RFI No :	BD-CW-SAMCO-PCO-RFI-MECH-004
Owner:	ROYA Developments	Rev. :	R00
Project Manager:	ACE-PM	Date :	08 / 03 / 2026
Consultant:	Prime Consultant		
Contractor:	SAMCO National Construction		
To:	PCO		

Coordination issues related to the cores/openings between basement 1 and basement 2

It has been observed that between Axis [26 and 27] and Axis [BB], the drain pipe serving the last toilet on the right side is currently passing directly through the storage room wall due to the location of the core provided in the slab.
Kindly advise whether this core location will be revised or if any modification to the pipe.

For the S-type toilets, it has been noted that the distance between the drain pipe core and the rear wall is not consistent across all toilets. Additionally, in some locations, the provided distance (**11 cm from the wall**) appears to be insufficient for proper fixture installation. Therefore, kindly confirm the required distance between the drain core of each fixture and the rear wall to ensure proper installation and coordination.

For your information, it has also been observed that some bathrooms are designed with S-type toilets, while other bathrooms are designed with P-type toilets.

Additionally, please note that in some locations, the cores may fall within structural caps

These notes raised to ensure proper coordination between the plumbing layout and the architectural/structural disciplines.

Attachments: Builder work drawing

For Contractor

Signature :

Date:

Supervision Consultant Response:

RE:

Signature :

Date:

Project Manager Response (If required)

ACEPM:

Signature

Date:

Distribution
CC

ACEPM

The Big

Request for Information (RFI)

Project:	The Big Business District	RFI No.:	BD-CW-SAMCO-PCO-RFI-MECH-005
Owner:	ROYA Developments	Rev.:	R1
Project Manager:	ACE-PM	Date:	08 / 03 / 2025
Consultant:	Prime Consultant		
Contractor:	SAMCO National Construction		
To:	PCO		

Subject

Clarifications Required for Latest Infrastructure Package

With reference to the latest issued Infrastructure Package, we would like to request clarification on the following points to ensure proper coordination prior to execution.

1) Irrigation Line – Level & Location Confirmation:

As per the latest infrastructure package, an irrigation line is indicated; however, the exact level and location are not clearly defined. Additionally, it should be noted that this irrigation line was not included in the previously issued mechanical package.

Kindly confirm whether the currently indicated location is final and approved, or if it is subject to modification.

This clarification is required since the irrigation line location will directly affect the installation of the sleeves / puddle flanges through the water tank walls.

Therefore, confirming the final level and location is essential to proceed with the required penetrations and avoid any potential rework.

2) Firefighting Line from Pump Room – Diameter & Level Clarification:

As per the latest infrastructure package, a firefighting line with a diameter of 315 mm is shown exiting the pump room and passing outside the retaining wall.

However, the invert level of this line is not indicated in the drawings.

Additionally, this line was not shown in the previously issued mechanical package, where only one **150 mm** line was indicated to serve Basement 1, Basement 2, and the buildings above.

Therefore, kindly clarify the following:

Confirm the required level of the **315 mm** firefighting line.

Confirm whether this line represents a new addition or a revision to the previous design.

Confirm the exact location and requirements for the wall penetration.

This clarification is required as it will directly affect the sleeve size and location to be provided in the pump room wall.

3) Infrastructure Drainage Pipes – Invert Level Coordination:

Regarding the infrastructure drainage lines, it has been observed that the invert levels of some external manholes to which these pipes are intended to connect appear to be higher than the invert levels of the corresponding drainage pipes.

This condition may prevent proper gravity flow connection to the manholes.

Kindly review and clarify the correct invert levels and connection details.

This clarification is essential as it will directly affect the location and level of the sleeves required through the retaining wall.

4) Water Supply Line Filling the Tanks – Location & Level Confirmation:

Regarding the water supply line filling the two tanks from the infrastructure network, it has been observed that this line was **110 mm** in the latest mechanical package.

However, in the infrastructure package, this line is indicated with a diameter of **200 mm**.

Therefore, kindly confirm the exact location and level of this line and also the diameter of the 2 pipes filling the each tank to allow proper coordination and to determine the required sleeves through the retaining wall.

Attachments

For Contractors

Signature :

Date:

Supervision Consultant Response

RE:

Signature :

Date:

Project Manager Response (If required)

ACEPM:

Signature

Date:

Distribution
CC

ACEPM

The Big

Request for Information (RFI)

Project:	The Big Business District
Owner:	ROYA Developments
Project Manager:	ACE-PM
Consultant:	Prime Consultant
Contractor:	SAMCO National Construction
To:	PCO

RFI No :	BD-CW-SAMCO-PCO-RFI-MECH-006
Rev. :	R00
Date :	26/3/2026

Subject

Pump Room Coordination Issues (Crane Clearance)

With reference to your response to RFI No. [BD-CW-SAMCO-PCO-RFI-MECH-002-R00], we would like to highlight the following point:

1) Crane Position & Clearance:

As per the latest mechanical package received, the pump room floor level is **199.05 m**.

Considering that the area for lifting, lowering, and handling of the pumps using the crane is located at the SOG of the curb, and the level of the curb is **205.15 m**.

Accordingly, the vertical distance between the pump room floor level and the curb level is **6.10 m**.

Furthermore, since the ramp forms the upper boundary of the pump room at this location, the total height of the pump room at this point is **9.335 m**.

Based on the above, the remaining clear height between the curb level and the ramp is approximately **3.23 m**.

Considering the dimensions of the pumps attached in your previous response (**2.5 m height**) and the height of the girder and hook (**1.5 m height**), the total required vertical clearance will be approximately **4.0 m**.

It is noted that this required clearance is not achieved

Attachments: 1 (A3) Sheet for pump room crane clearance section

For Contractor



Signature : _____

Date: _____

**Supervision Consultant Response:**

RE: _____

Signature : _____

Date: _____

Project Manager Response (If required)

ACEPM: _____

Signature _____

Date: _____

Distribution
CC :

ACEPM
